

BU5300 – IT Project Management


IT Project Management

Lecture 9: **Stakeholder Management and Leadership**

Chapters 18 and 21

Overview of the Course

Lectures and Book Chapters



Lecture 1 - Chapters 1 and 2

Lecture 2 - Chapters 3 and 4

Lecture 3 - Chapter 6

Lecture 4 - *Agile Development*

Lecture 5 - Chapters 7 and 8

Lecture 6 - Chapter 9 and 10

Lecture 7 - Chapters 11 - 14

Lecture 8 - Chapter 15

Lecture 9 - Chapters 18 and 21

Lecture 10 - Chapters 20, 22 and 23

IMPORTANT! Changes may occur. Always check on Canvas and TimeEdit

Chapter 18: Stakeholder Analysis

Learning Outcomes

- Identify an organization's and a project's stakeholders
- Prepare a stakeholder map
- List different approaches for managing different stakeholders
- Describe a process for resolving conflict between stakeholders
- Follow guidelines to build good stakeholder relationships

Stakeholders


For organizations

- Individuals and groups who are affected by the activities of an organization
- Internal and External

For a Project

- People interested in the project
- PMs should identify the stakeholders
- Plan how to involve and communicate with stakeholders

Organization Stakeholders

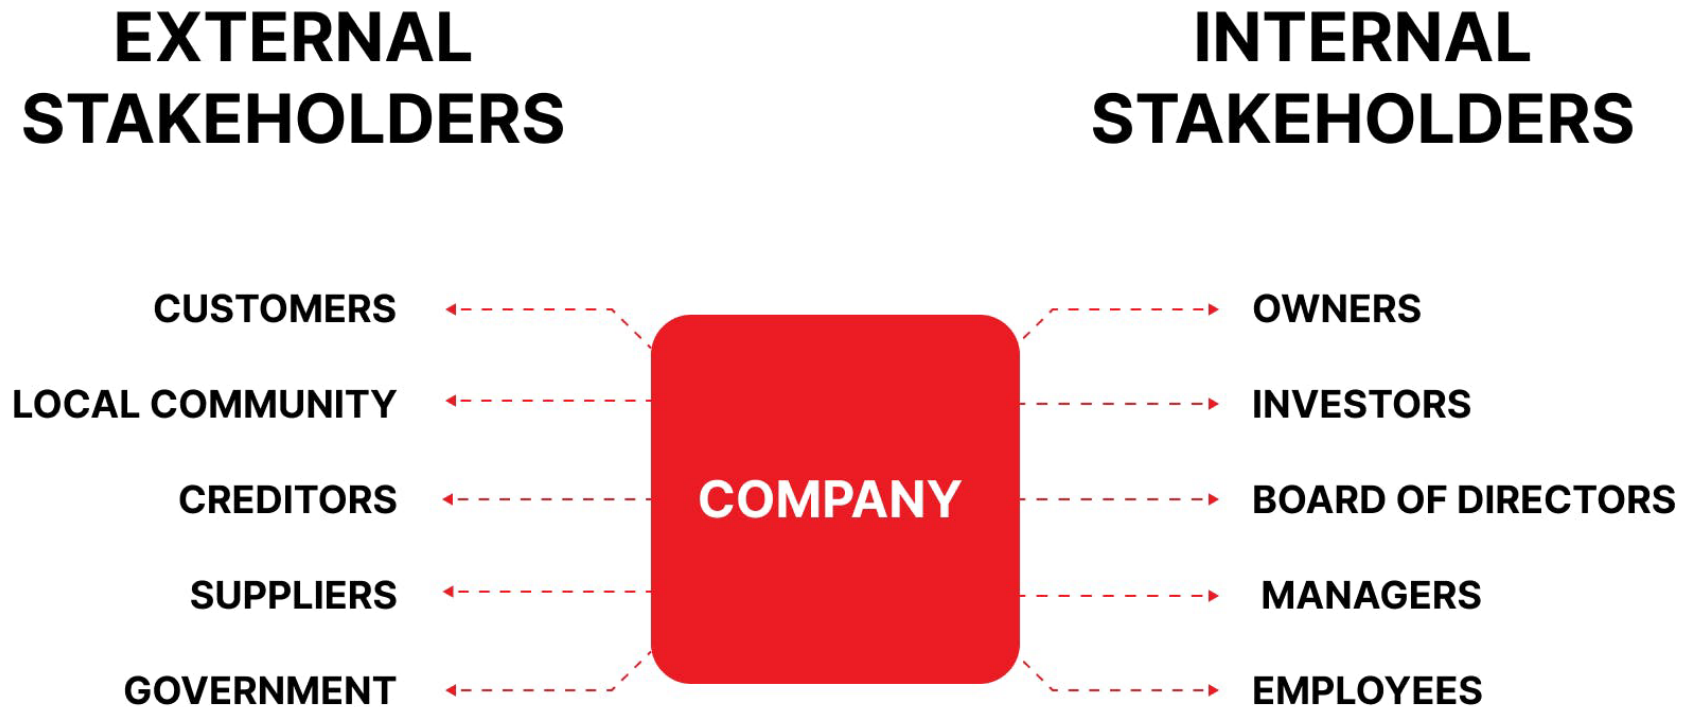

Project Stakeholders

Who should be involved and how?

- **Who are** the key stakeholders of the project?
- **What influence and expectations** do different stakeholders have for our project?
- What influence do we have as project managers?

Agreeing on success criteria with all the stakeholders is an important determinant of project success

Key stakeholders


- can influence the project to a great extent
- have expectations for the result
- may have the power to end the project
- may have important information about user needs and the context in which a new IT system will be used



Stakeholder analysis

Three main steps:

1. Identify stakeholders
2. Analyze the influence and expectations
 - Or power and interest
3. Create an overall strategy for communicating and influencing different stakeholders
 - Project stakeholder management (PSM) strategy

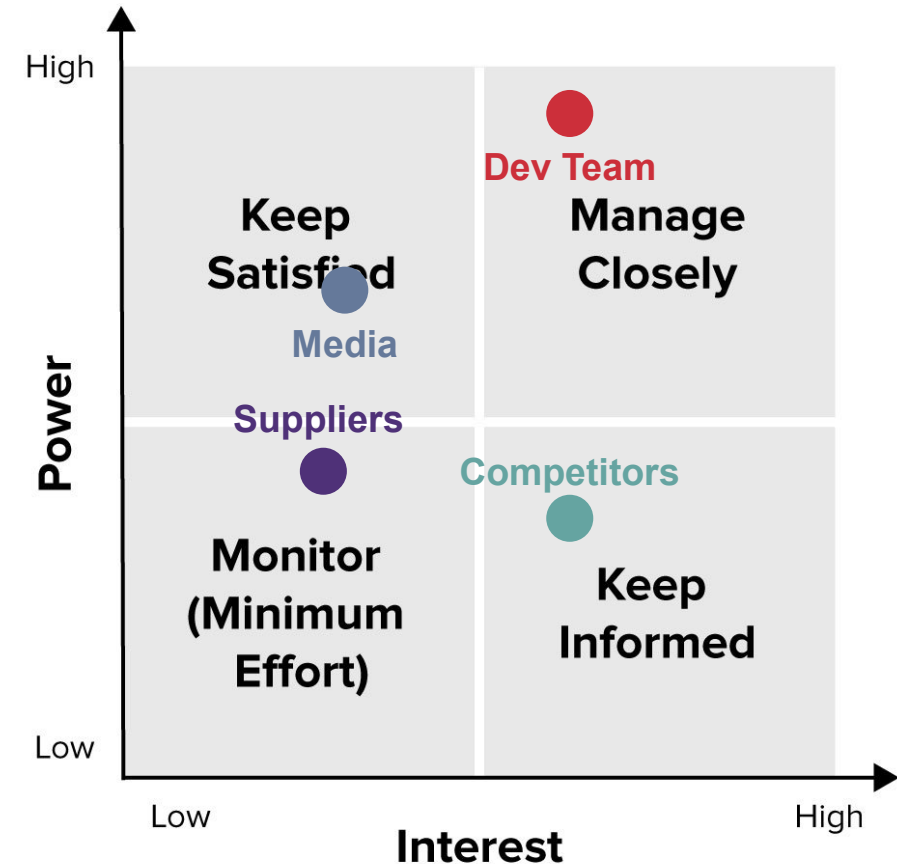

Examples of stakeholders

Developing a mobile application

Stakeholder	Interest	Power	Expectations	Engagement/communications
Project Sponsor	High	High	Clear project goals and milestones, regular progress updates	Keep informed, involve in key decision-making
End-users (customers)	High	High	User-friendly and intuitive app design, reliable and efficient app performance	Conduct user research, involve in app design and testing
Competitors	High	Low	Monitor and analyse their app features and marketing strategies	Stay informed and adapt as necessary
Regulatory bodies (e.g. Datatilsynet)	High	High	App complies with relevant laws and regulations, user data is protected	Ensure app complies with relevant laws and regulations
Media	Low	High	Positive media coverage and accurate reporting	Establish positive relationships, provide regular updates, respond promptly to media inquiries

Examples of stakeholders, cont.

Developing a mobile application

Stakeholder	Interest	Power	Expectations	Engagement/communications
Dev Team	High	High	<i>Clear project requirements and timelines, opportunities for learning and growth</i>	<i>Involve in project planning, provide regular updates and feedback</i>
Other employees	Low	Low	<i>Clear project impact on their work, opportunities for involvement and feedback</i>	<i>Keep informed of project progress and how it may affect their work</i>
App Store	High	High	App meets their guidelines and standards, positive user ratings and reviews	Ensure app meets their guidelines and standards
Service Providers (e.g. AWS, Vipps)	Medium	Low	Reliable and cost-effective service, timely issue resolution	Ensure contracts are in place and service levels are met
Suppliers	Low	Low	Reliable and cost-effective supply of necessary resources	Ensure reliable and cost-effective supply of necessary resources

Deciding on the appropriate course of action

The following question can help:

- How can we influence this group of stakeholders to support the project?
- What kind of support do we want from them?
- What will the project deliver to meet their concerns?
- How could they demonstrate their lack of support? What recourse do we have if this occurs?

Project manager's role

- Reach your project goals in terms of budget, quality and time
- Ensure that the project has the right expertise
- Establish teams and motivate good efforts
- Managing conflicts and communication within the team and between teams around the outside world
- Plan and track your project
- Make decisions

Conflict management

Sources of conflict

- Different expectations
- Interruptions and the inability to keep to the original timescale
- Lack of understanding of each other's position
- Issues that have been left unresolved or avoided come back at a critical point and can no longer be ignored
- Physical distances, proximity and culture

Resolving conflict

- Know your desired outcome
- Triage the conflict
 - sort through the issues surrounding a conflict to decide which are critical and which may be peripheral
- Agree a process
- Confirm the positions
- Take action!

Chapter 21: Leadership

Learning outcomes

- Recognize the need for leadership
- Describe some key leadership styles and behaviors
- Set clear objectives for the people who work for you
- Review the performance of others
- Prepare for dealing with poor performance
- Identify an appropriate level of balance for the direction and support of team members

Leaders vs Managers

What's the difference?

Managers

- are rather impersonal about goals: for them, goals are organizational and not personal
- coordinate and balance activities to meet conflicting schedules
- maintain a greater distance

Leaders

- take on a personal commitment and are very active about their goals
- create excitement and change and enjoy the uncertainty
- are emotionally involved with their people

Leadership


- Achieving team objectives
- Defining tasks
- Planning work
- Allocating resources
- Assigning responsibilities
- Monitoring progress
- Controlling quality

- SETTING OBJECTIVES
- PLANNING TASKS
- ALLOCATING OF RESPONSIBILITIES
- SETTING PERFORMANCE STANDARDS




- Easy to get too preoccupied with the tasks and very little with people and teams
 - Many developers are motivated by the tasks themselves
- Do not forget to building teams and making sure that individuals have motivating tasks

The waterfall model and management style

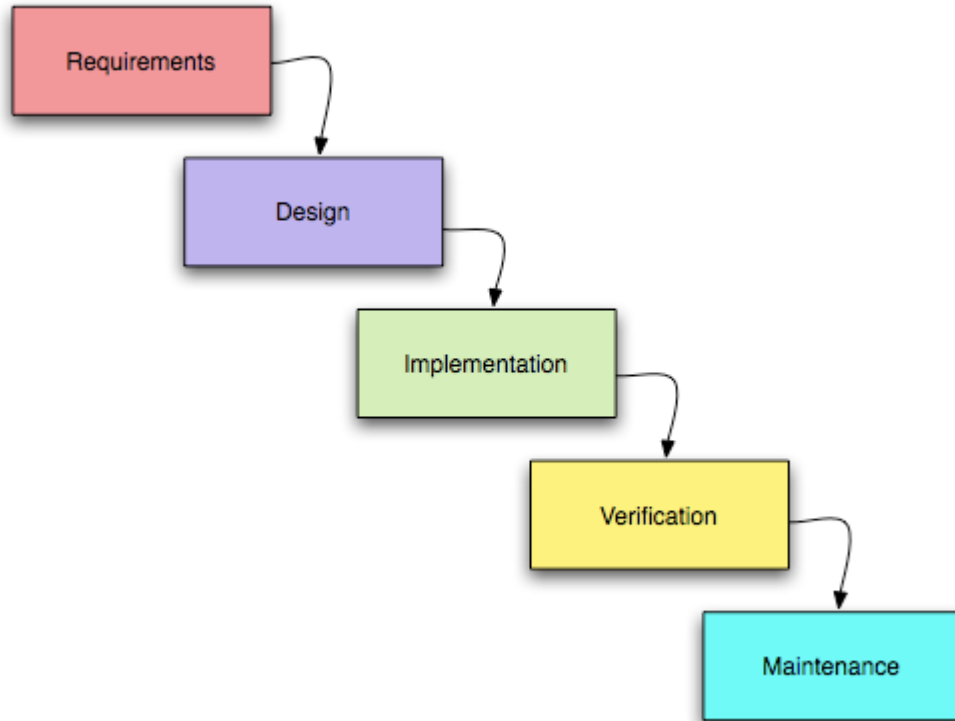

- Waterfall models focus mostly on overall tasks and a little on individuals
- No focus on teams
- What consequences does this have?
- How can we compensate?


Agile leadership

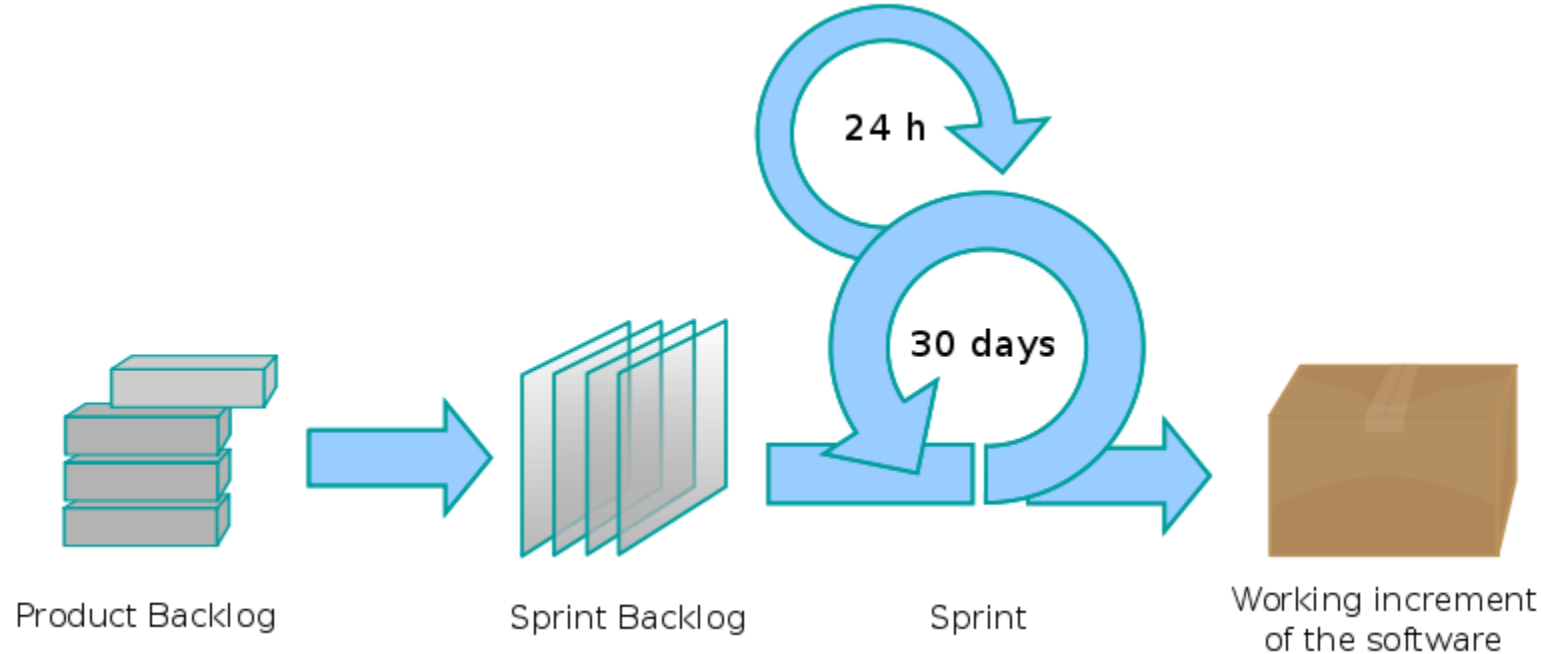

Agile methods typically have a greater focus on teams and tasks relate to the requirements. Less on individual! What consequences can this have?

Leadership styles


Tannenbaum and Schmidt Continuum of Leadership

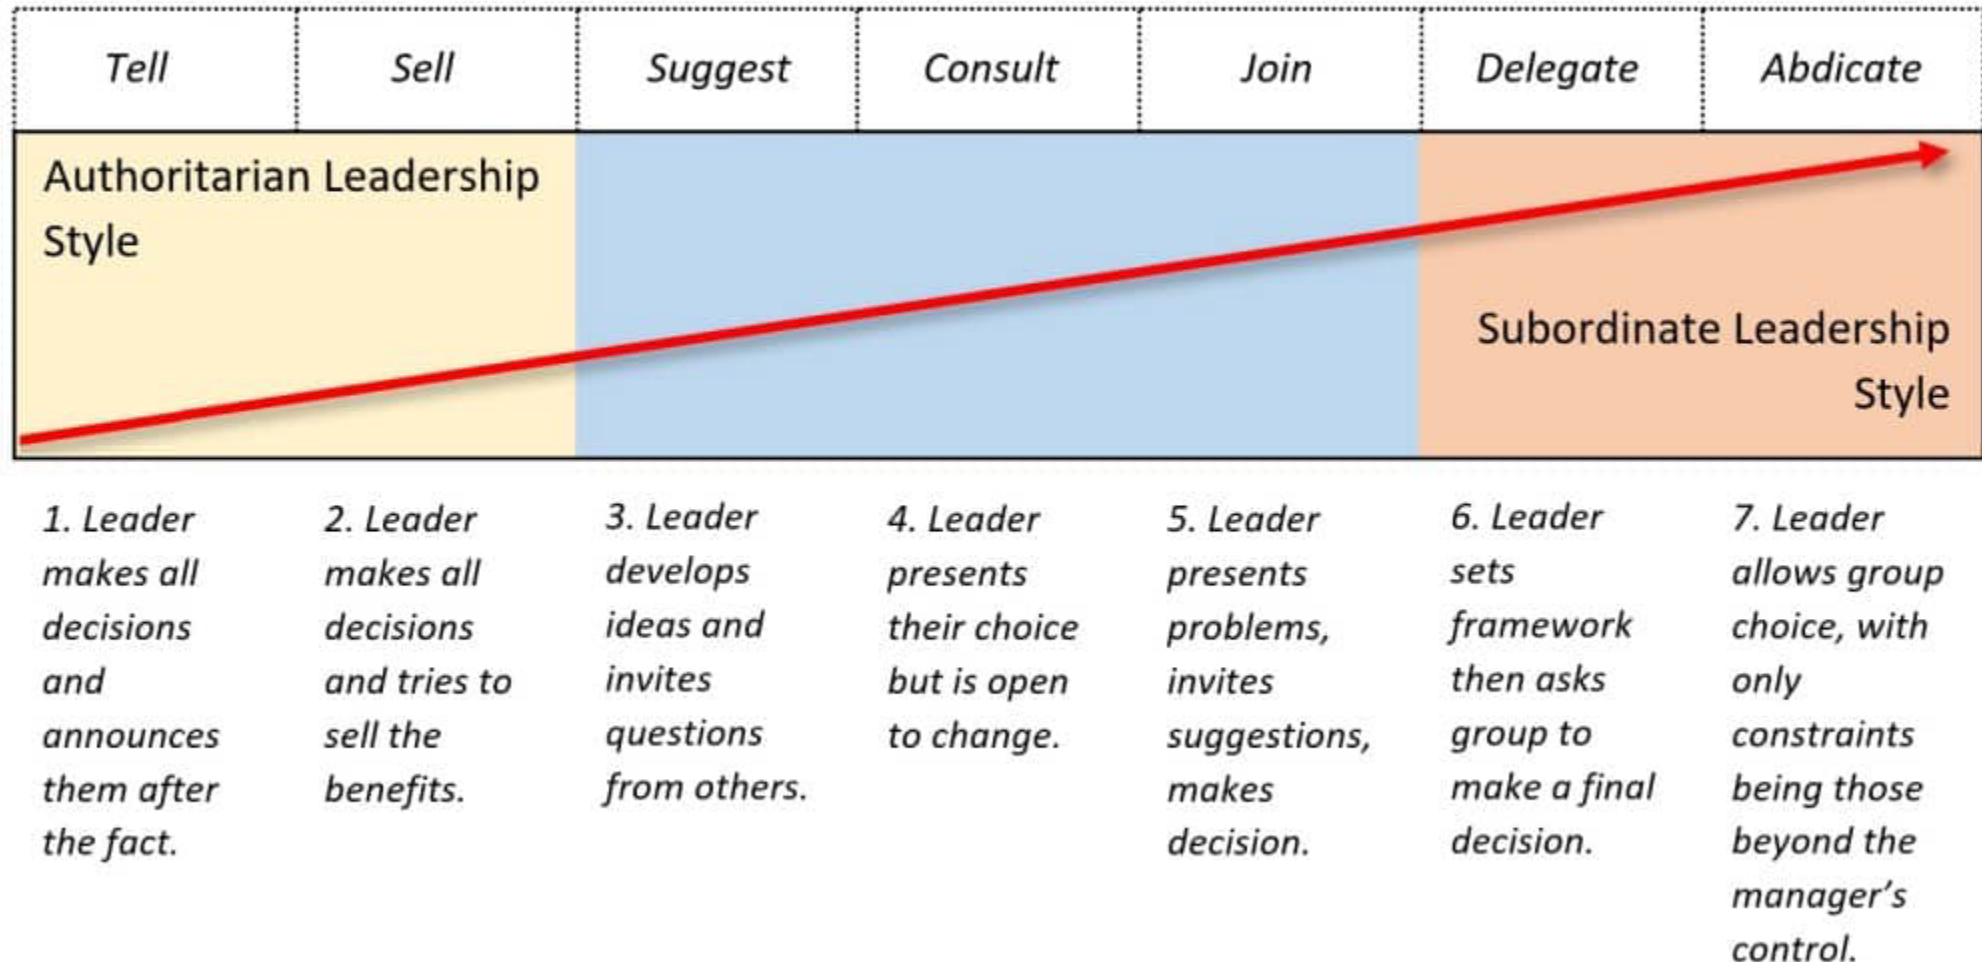

Leadership styles

- Development Level and Leadership Style
 - What are we doing? **Directing**
 - Why are we doing this? **Coaching**
 - We think... **Supporting**
 - What's next? **Delegating**

<https://situational.com/situational-leadership/>

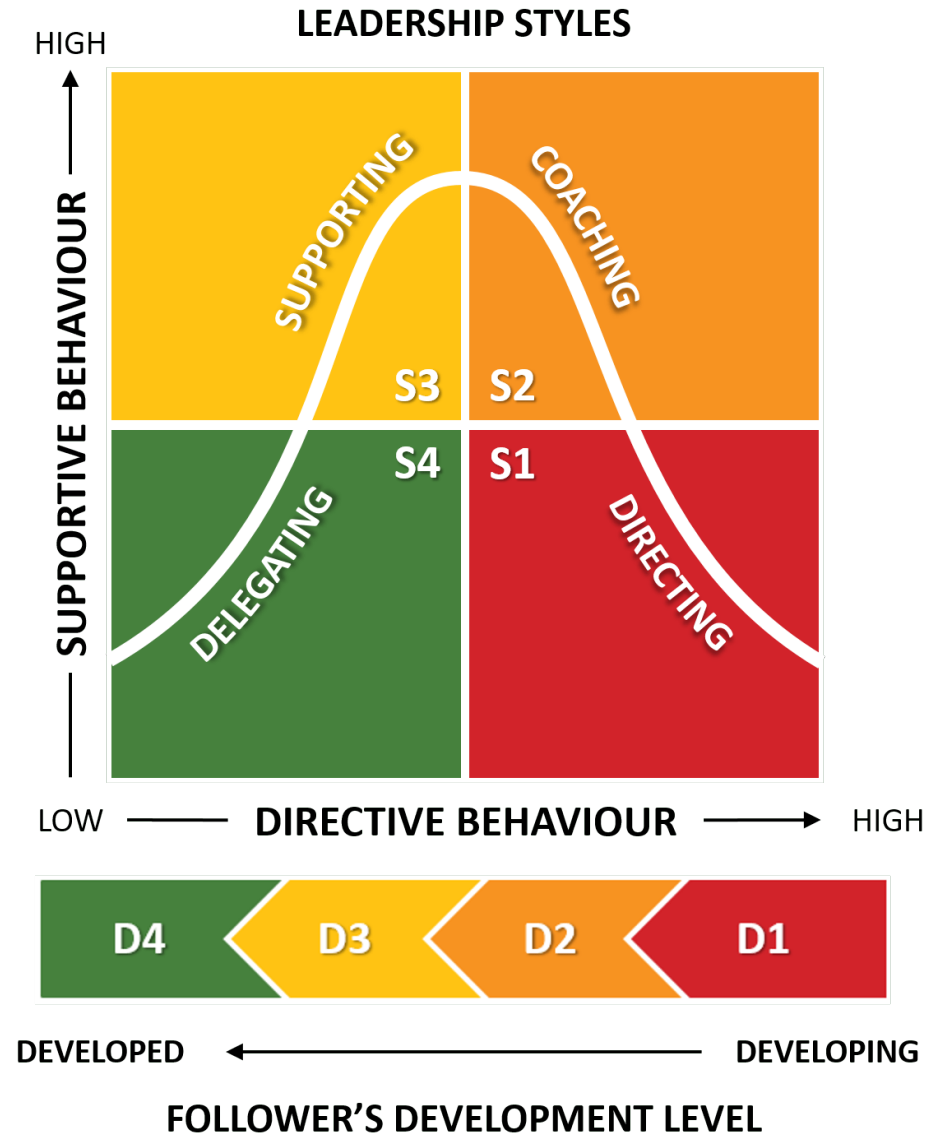

Leadership style

- Must be adapted to the team, competence, organization and type of project
- Many developers like to take command and provide clear guidelines
- Many designers resent taking command

Key activities for a leader

Team Management

- Different roles: team role and a functional role
- Typically needs to adjust roles over time
- The role of the project manager to make sure to balance one or some dominant people in the team
- A lot of focus and time to establish the team at the start of the project
- Review the phases and tasks
- Important to maintain some discussion
- Avoid group thinking

Management of highly competent professionals

- Don't take the expert role
 - Remember that it's the team members who are experts
- Familiarize yourself with what team members do and what their expertise is
- Use team members to make decisions that matches their expertise
 - But don't let them dictate the direction of the project

Conflict within the team

- Arrange a meeting between the parties
- Listen to what everyone has to say
- Remember that it is easy to hurt people who have worked hard for a long time
- Give people a chance – but give clear feedback and decisions
- As a project manager, you should to some extent protect team members from the noise outside the project

New team members

- Must start over with team creation every time you replace members
- It is often easier to bring in two new ones that are coordinated in front of an individual
- Lack of domain knowledge in new ones can be both a disadvantage and an advantage
- And about switching team members?

Importance of co-location

- Team members get to know each other faster – good for learning
- As a project manager, you should sit with your team
- Some disadvantages of co-location – companies with game rules

Questions?

Jefferson Seide Molléri
jefferson.molleri@Kristiania.no

Exercise

- Create a stakeholder analysis of your designated project
 - Identify the key stakeholders, both internal and external ones
 - Describe what are the expectations each stakeholder
 - Detail their power (influence) and interest
 - Define engagement strategies / communication channels
- **Note:** create explicit links/references to the progress report, risk assessment and other previous steps

Bibliography

- Cadle, James, and Donald Yeates, eds. **Project management for information systems**. Pearson education, 2004.
- Tannenbaum, Robert, and Warren H. Schmidt. **How to choose a leadership pattern**. Leadership perspectives. Routledge, 2017. 75-84.
- Heresy, Paul, and Kenneth Blanchard. **Management of organization. Behavior: Utilizing Human Resource**. Prentice-Hall, 2001.
